


ID	%	Task Name	Duration	Predecessors	Start	Finish	2012				2013				2014				2015				2016				2017
							Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4
1	99%	Contract Design Firms	450 days		Tue 11/1/11	Mon 7/22/13																					
2	100%	Finalize Project Scope	550 days	1	Tue 7/23/13	Mon 8/31/15																					
3	100%	Preliminary Alignment	300 days	2	Tue 9/1/15	Mon 10/24/16																					
4	37%	NEPA	1352 days	2	Sun 11/1/15	Tue 1/5/21																					
5	100%	Execute Agreement with	200 days	3	Tue 10/25/16	Fri 9/8/17																					
6	100%	Finalize Functional Plans	100 days	3	Tue 10/25/16	Mon 3/13/17																					
7	100%	Right Of Way Acquisition	347 days	6	Tue 3/14/17	Wed 7/11/18																					
8	0%	Relocate Utilities	100 days	6,4,7	Wed 1/6/21	Tue 5/25/21																					
9	70%	STIP/TIP Approval	90 days		Wed 1/1/20	Tue 5/5/20																					
10	0%	Finalize Design Plans	71 days	6	Wed 6/1/22	Wed 9/7/22																					
11	0%	Submit PS&E	30 days	10	Thu 9/8/22	Wed 10/19/22																					
12	0%	Contracting for	150 days	11,8	Thu 10/20/22	Wed 5/17/23																					
13	0%	Reconstruct Douglas	800 days	12	Thu 5/18/23	Wed 6/10/26																					
14	0%	Raise Westminster Road	60 days	12	Thu 5/18/23	Wed 8/9/23																					
15	0%	Construct center of new	150 days	12	Thu 5/18/23	Wed 12/13/23																					
16	0%	Build Inside Shoulder	200 days	12	Thu 5/18/23	Wed 2/21/24																					
17	0%	Construct WB lanes on	120 days	15,16,14	Thu 2/22/24	Wed 8/7/24																					
18	0%	Reconstruct Westbound	300 days	15,14,16	Thu 2/22/24	Wed 4/16/25																					
19	0%	Construct EB lanes on	120 days	12,18,17	Thu 4/17/25	Wed 10/1/25																					
20	0%	Reconstruct Eastbound	300 days	18,17	Thu 4/17/25	Wed 6/10/26																					

Project: 2020.02.19 CPM.mpp  
Date: Wed 2/19/20

Task		External Tasks		Manual Task		Finish-only		Slippage	
Split		External Milestone		Duration-only		Deadline			
Milestone		Inactive Task		Manual Summary Rollup		Critical			
Summary		Inactive Milestone		Manual Summary		Critical Split			
Project Summary		Inactive Summary		Start-only		Progress			

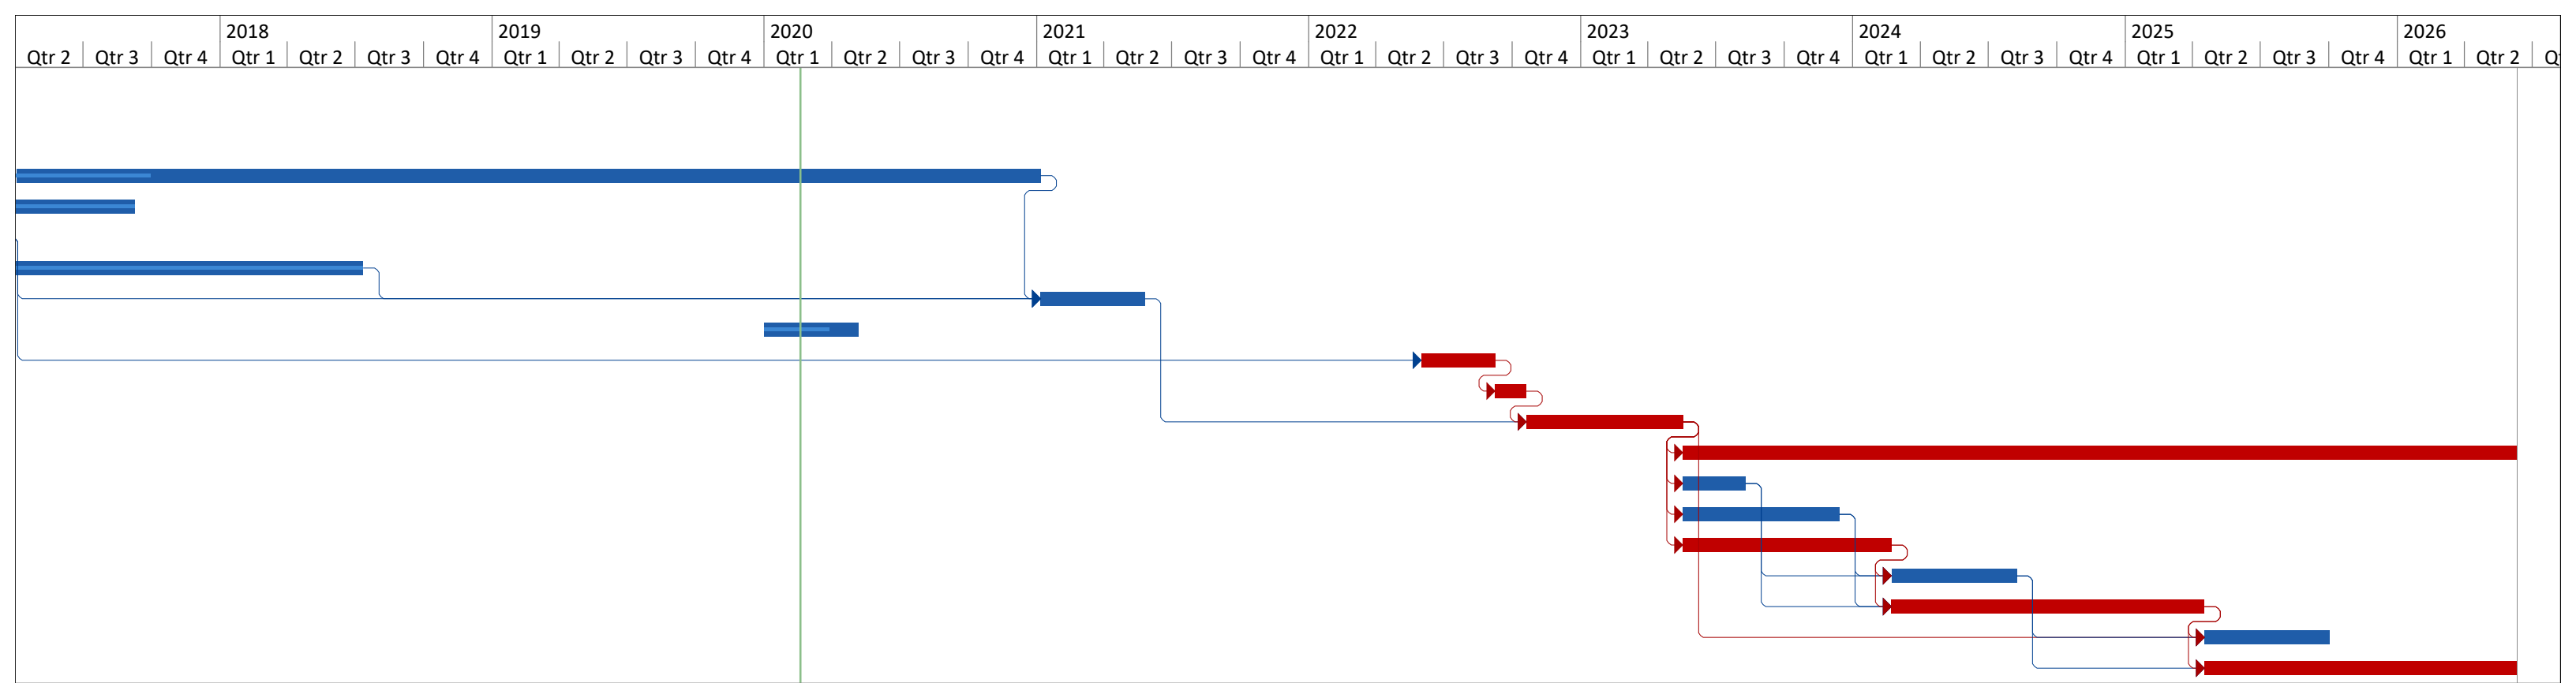

Project: 2020.02.19 CPM.mpp  
Date: Wed 2/19/20

Task		External Tasks		Manual Task		Finish-only		Slippage	
Split		External Milestone		Duration-only		Deadline			
Milestone		Inactive Task		Manual Summary Rollup		Critical			
Summary		Inactive Milestone		Manual Summary		Critical Split			
Project Summary		Inactive Summary		Start-only		Progress			
