ID	% Complete	Task Name	Duration	Start	Finish
1	100%	Contract Design Firms	450 days	Tue 11/1/11	Mon 7/22/13
2	100%	Finalize Project Scope	550 days	Tue 7/23/13	Mon 8/31/15
3	100%	Preliminary Alignment	349 days	Tue 9/1/15	Fri 12/30/16
4	100%	NEPA	1000 days	Sun 11/1/15	Fri 8/30/19
5	100%	Execute Agreement with Oklahoma	200 days	Tue 10/25/16	Fri 9/8/17
6	100%	Finalize Functional Plans	100 days	Tue 10/25/16	Mon 3/13/17
7	100%	Right Of Way Acquisition	660 days	Tue 3/14/17	Mon 9/23/19
8	90%	Relocate Utilities	485 days	Tue 9/24/19	Mon 8/2/21
9	85%	Finalize Design Plans	1200 days	Tue 3/14/17	Mon 10/18/21
10	70%	STIP/TIP Approval	90 days	Wed 9/1/21	Tue 1/4/22
11	0%	Submit PS&E and Obligate Funds	60 days	Tue 10/19/21	Mon 1/10/22
12	0%	Contracting for Construction	90 days	Tue 1/11/22	Mon 5/16/22
13	**0%**	**Construct Bypass**	**1200 days**	**Tue 5/17/22**	**Mon 12/21/26**
14	0%	Grading for bypass	700 days	Tue 5/17/22	Mon 1/20/25
15	0%	Construct new bridges along bypass	300 days	Tue 1/21/25	Mon 3/16/26
16	0%	Contruct 2 lane roadway	300 days	Tue 1/21/25	Mon 3/16/26
17	0%	Tie in local roads with ramps	200 days	Tue 3/17/26	Mon 12/21/26

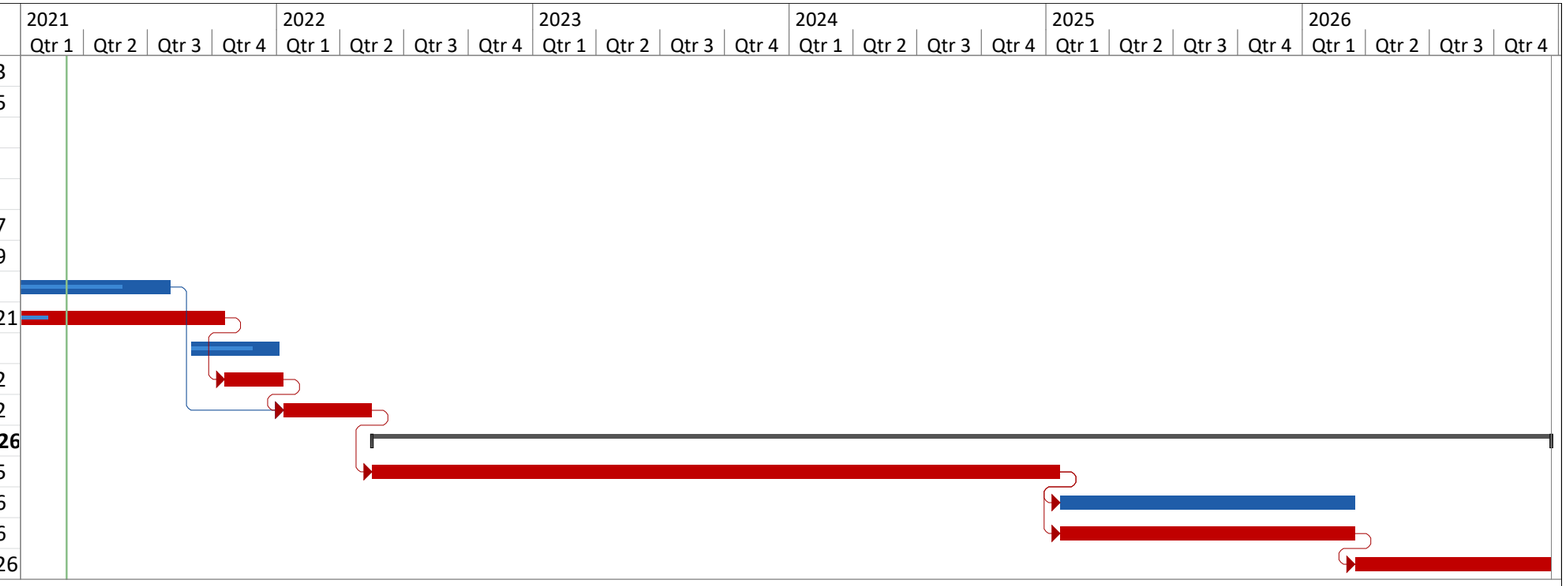

Project: 2020.02.20 - Schedule.mp
Date: Mon 3/8/21

Task	External Tasks	Manual Task	Finish-only	Slippage
Split	External Milestone	Duration-only	Deadline	
Milestone	Inactive Task	Manual Summary Rollup	Critical	
Summary	Inactive Milestone	Manual Summary	Critical Split	
Project Summary	Inactive Summary	Start-only	Progress	
